


Cadman and Adderley Pre Contract Programme

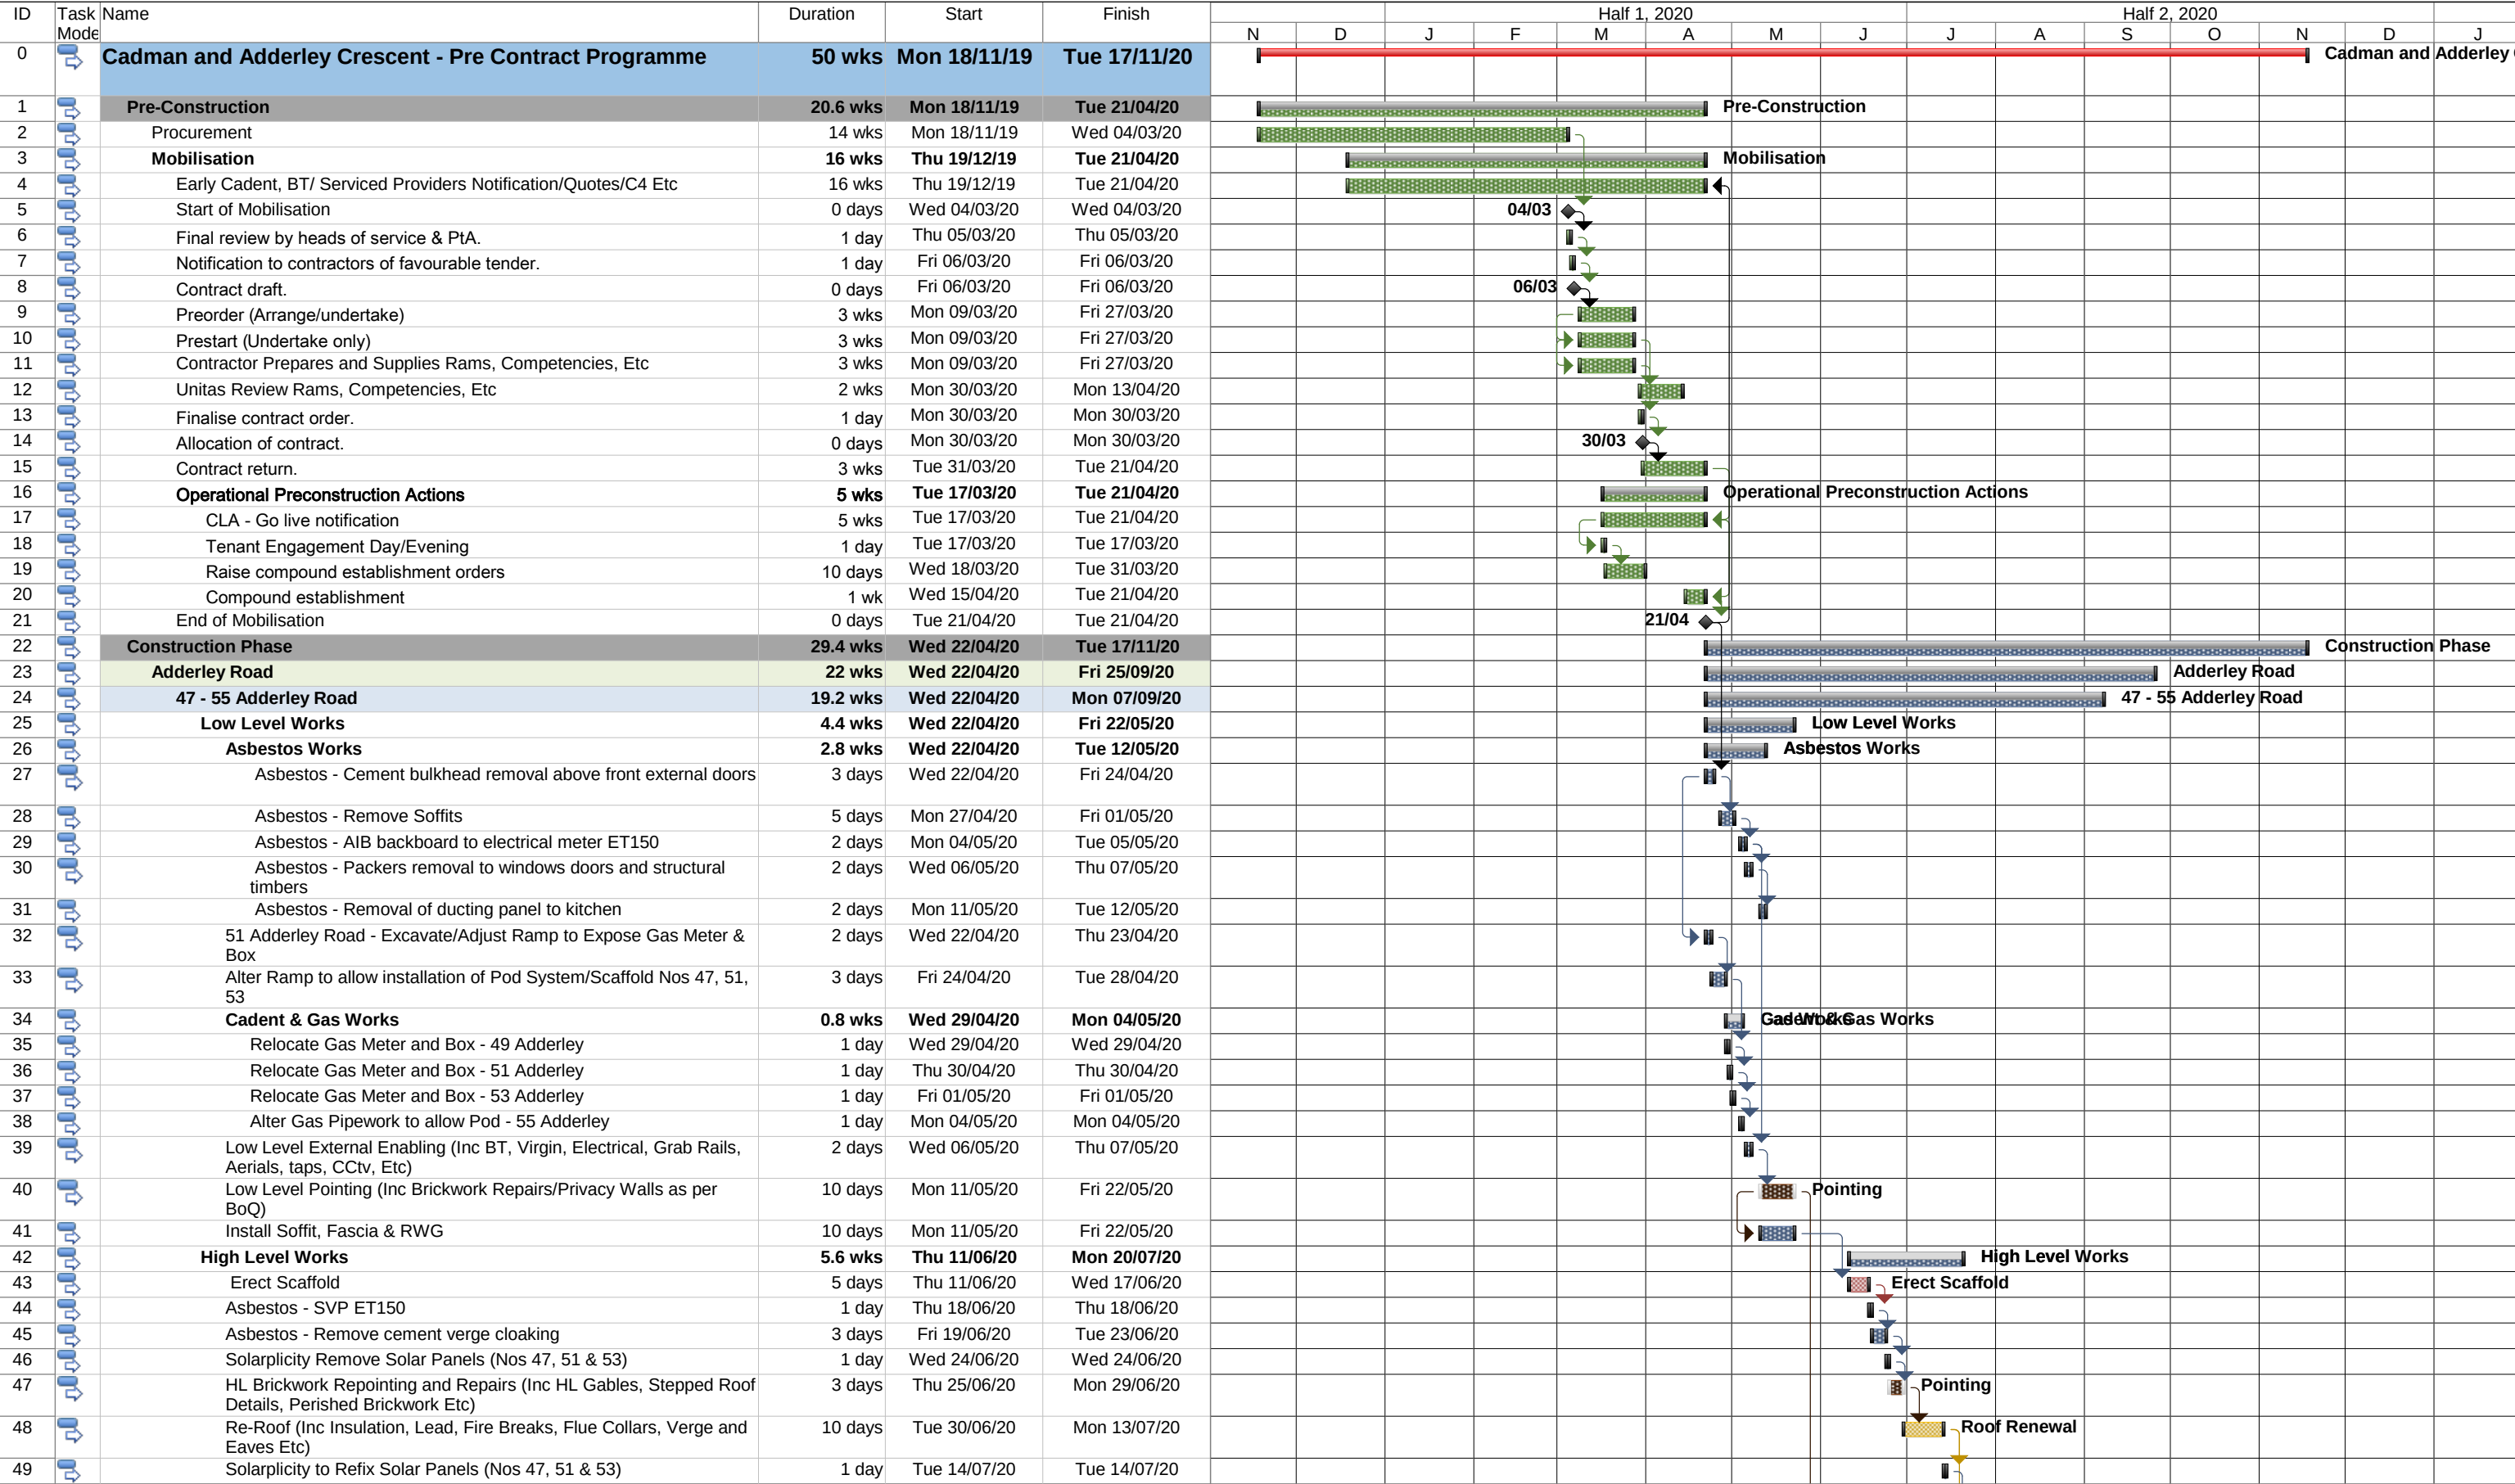

Project: Cadman and Adderley Cresce
Date: Mon 11/11/19

Mobilisation/Pre Con

General Construction

Pointing

Scaffolding

Roofing

Pod System

Milestone

Summary

◆

◆

Rolled Up Progress

Project Summary

Group By Summary

Progress

Cadman and Adderley Pre Contract Programme



ID	Task Name	Mode	Duration	Start	Finish	Half 1, 2020							Half 2, 2020								
						N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	
50	Strike Scaffold		4 days	Wed 15/07/20	Mon 20/07/20											Strike Scaffold					
51	Pods, Kitchens and Bathrooms		2 wks	Wed 05/08/20	Tue 18/08/20											Pods, Kitchens and Bathrooms					
52	47 Adderley Road		0.4 wks	Wed 05/08/20	Thu 06/08/20											47 Adderley Road					
53	Remove Front Façade, Install SFS Frame, External Weatherboarding, Window Frames and External Door		1 day	Wed 05/08/20	Wed 05/08/20											Pod System					
54	Remove Rear Façade, Install SFS Frame, External Weatherboarding, Window Frames and External Door		1 day	Thu 06/08/20	Thu 06/08/20											Pod System					
55	49 Adderley Road		0.4 wks	Fri 07/08/20	Mon 10/08/20											49 Adderley Road					
56	Remove Front Façade, Install SFS Frame, External Weatherboarding, Window Frames and External Door		1 day	Fri 07/08/20	Fri 07/08/20											Pod System					
57	Remove Rear Façade, Install SFS Frame, External Weatherboarding, Window Frames and External Door		1 day	Mon 10/08/20	Mon 10/08/20											Pod System					
58	51 Adderley Road - Ramp		0.4 wks	Tue 11/08/20	Wed 12/08/20											51 Adderley Road - Ramp					
59	Remove Front Façade, Install SFS Frame, External Weatherboarding, Window Frames and External Door		1 day	Tue 11/08/20	Tue 11/08/20											Pod System					
60	Remove Rear Façade, Install SFS Frame, External Weatherboarding, Window Frames and External Door		1 day	Wed 12/08/20	Wed 12/08/20											Pod System					
61	53 Adderley Road		0.4 wks	Thu 13/08/20	Fri 14/08/20											53 Adderley Road					
62	Remove Front Façade, Install SFS Frame, External Weatherboarding, Window Frames and External Door		1 day	Thu 13/08/20	Thu 13/08/20											Pod System					
63	Remove Rear Façade, Install SFS Frame, External Weatherboarding, Window Frames and External Door		1 day	Fri 14/08/20	Fri 14/08/20											Pod System					
64	55 Adderley Road		0.4 wks	Mon 17/08/20	Tue 18/08/20											55 Adderley Road					
65	Remove Front Façade, Install SFS Frame, External Weatherboarding, Window Frames and External Door		1 day	Mon 17/08/20	Mon 17/08/20											Pod System					
66	Remove Rear Façade, Install SFS Frame, External Weatherboarding, Window Frames and External Door		1 day	Tue 18/08/20	Tue 18/08/20											Pod System					
67	Rain Defence External Pod Cladding		5 days	Mon 17/08/20	Fri 21/08/20											2nd Fix Pod External					
68	Install Multivent Fans & Ld2s		5 days	Mon 24/08/20	Fri 28/08/20											Electrical					
69	Internal Plastering, Carpentry and Decorating		5 days	Tue 01/09/20	Mon 07/09/20											2nd Fix Pods Internal					
70	External Security Lighting - 1 per property		3 days	Thu 03/09/20	Mon 07/09/20											Electrical					
71	Clean Gullies		3 days	Thu 03/09/20	Mon 07/09/20											Clean					
72	Clean and Clear Site		1 day	Mon 07/09/20	Mon 07/09/20											Clear Site					
73	57 - 67 Adderley Road		21.4 wks	Mon 27/04/20	Fri 25/09/20											57 - 67 Adderley Road					
74	Low Level Works		6.2 wks	Mon 27/04/20	Wed 10/06/20											Low Level Works					
75	Asbestos Works		3 wks	Mon 27/04/20	Tue 19/05/20											Asbestos Works					
76	Asbestos - Cement bulkhead removal above front external doors		3 days	Mon 27/04/20	Thu 30/04/20																
77	Asbestos - Remove Soffits		6 days	Thu 30/04/20	Mon 11/05/20																
78	Asbestos - AIB backboard to electrical meter ET150		2 days	Mon 11/05/20	Wed 13/05/20																
79	Asbestos - Packers removal to windows doors and structural timbers		2 days	Wed 13/05/20	Fri 15/05/20																
80	Asbestos - Removal of ducting panel to kitchen		2 days	Fri 15/05/20	Tue 19/05/20																
81	Cadent & Gas Works		0.4 wks	Tue 19/05/20	Thu 21/05/20											Cadent & Gas Works					
82	Alter Gas Pipework to allow Pod - 61 Adderley		1 day	Tue 19/05/20	Wed 20/05/20																
83	Relocate Gas Meter and Box - 63 Adderley		1 day	Wed 20/05/20	Thu 21/05/20																
84	Low Level External Enabling (Inc BT, Virgin, Electrical, Grab Rails, Aerials, taps, CCtv, Etc)		2 days	Thu 21/05/20	Tue 26/05/20																
85	Low Level Pointing (Inc Brickwork Repairs/Privacy Walls as per BoQ)		12 days	Tue 26/05/20	Wed 10/06/20											Pointing					
86	Install Soffit, Fascia & RWG		12 days	Tue 26/05/20	Wed 10/06/20																
87	High Level Works		6.6 wks	Tue 23/06/20	Thu 06/08/20											High Level Works					
88	Erect Scaffold		6 days	Tue 23/06/20	Wed 01/07/20											Erect Scaffold					
89	Asbestos - SVP ET150		1 day	Wed 01/07/20	Thu 02/07/20																
90	Asbestos - Remove cement verge cloaking		3 days	Thu 02/07/20	Tue 07/07/20																
91	Solarplicity Remove Solar Panels (Nos 61 & 67)		1 day	Tue 07/07/20	Wed 08/07/20																
92	HL Brickwork Repointing and Repairs (Inc HL Gables, Stepped Roof Details, Perished Brickwork Etc)		4 days	Wed 08/07/20	Tue 14/07/20											Pointing					
93	Re-Roof (Inc Insulation, Lead, Fire Breaks, Flue Collars, Verge and Eaves Etc)		12 days	Tue 14/07/20	Wed 29/07/20											Roof Renewal					
94	Solarplicity to Refix Solar Panels (Nos 61 & 67)		1 day	Thu 30/07/20	Thu 30/07/20																
95	Strike Scaffold		5 days	Fri 31/07/20	Thu 06/08/20											Strike Scaffold					

Project: Cadman and Adderley Cresce
Date: Mon 11/11/19

Mobilisation/Pre Con

General Construction

Pointing

Scaffolding

Roofing

Pod System

Milestone

Summary

◆

◆

Rolled Up Progress

Project Summary

Group By Summary

Progress

Cadman and Adderley Pre Contract Programme



ID	Task Mode	Name	Duration	Start	Finish	Half 1, 2020								Half 2, 2020						
						N	D	J	F	M	A	M	J	J	A	S	O	N	D	J
96		Pods, Kitchens and Bathrooms	3.2 wks	Wed 19/08/20	Thu 10/09/20											Pods, Kitchens and Bathrooms				
97		57 Adderley Road	0.4 wks	Wed 19/08/20	Thu 20/08/20											57 Adderley Road				
98		Remove Front Façade, Install SFS Frame, External Weatherboarding, Window Frames and External Door	1 day	Wed 19/08/20	Wed 19/08/20											Pod System				
99		Remove Rear Façade, Install SFS Frame, External Weatherboarding, Window Frames and External Door	1 day	Thu 20/08/20	Thu 20/08/20											Pod System				
100		59 Adderley Road	0.4 wks	Fri 21/08/20	Mon 24/08/20											59 Adderley Road				
101		Remove Front Façade, Install SFS Frame, External Weatherboarding, Window Frames and External Door	1 day	Fri 21/08/20	Fri 21/08/20											Pod System				
102		Remove Rear Façade, Install SFS Frame, External Weatherboarding, Window Frames and External Door	1 day	Mon 24/08/20	Mon 24/08/20											Pod System				
103		61 Adderley Road	1.2 wks	Tue 25/08/20	Wed 02/09/20											61 Adderley Road				
104		Remove Front Façade, Install SFS Frame, External Weatherboarding, Window Frames and External Door	1 day	Tue 25/08/20	Tue 25/08/20											Pod System				
105		Remove Rear Façade, Install SFS Frame, External Weatherboarding, Window Frames and External Door	1 day	Wed 26/08/20	Wed 26/08/20											Pod System				
106		Renew Bathroom	4 days	Thu 27/08/20	Wed 02/09/20											Pod System				
107		63 Adderley Road	2 wks	Thu 27/08/20	Thu 10/09/20											63 Adderley Road				
108		Remove Front Façade, Install SFS Frame, External Weatherboarding, Window Frames and External Door	1 day	Thu 27/08/20	Thu 27/08/20											Pod System				
109		Remove Rear Façade, Install SFS Frame, External Weatherboarding, Window Frames and External Door	1 day	Fri 28/08/20	Fri 28/08/20											Pod System				
110		Renew Kitchen	4 days	Tue 01/09/20	Fri 04/09/20											Pod System				
111		Renew Bathroom	4 days	Mon 07/09/20	Thu 10/09/20											Pod System				
112		65 Adderley Road	0.4 wks	Tue 01/09/20	Wed 02/09/20											65 Adderley Road				
113		Remove Front Façade, Install SFS Frame, External Weatherboarding, Window Frames and External Door	1 day	Tue 01/09/20	Tue 01/09/20											Pod System				
114		Remove Rear Façade, Install SFS Frame, External Weatherboarding, Window Frames and External Door	1 day	Wed 02/09/20	Wed 02/09/20											Pod System				
115		67 Adderley Road	0.4 wks	Thu 03/09/20	Fri 04/09/20											67 Adderley Road				
116		Remove Front Façade, Install SFS Frame, External Weatherboarding, Window Frames and External Door	1 day	Thu 03/09/20	Thu 03/09/20											Pod System				
117		Remove Rear Façade, Install SFS Frame, External Weatherboarding, Window Frames and External Door	1 day	Fri 04/09/20	Fri 04/09/20											Pod System				
118		Install Multivent Fans & Ld2s	5 days	Mon 07/09/20	Fri 11/09/20											2nd Fix Pod External				
119		Rain Defence External Pod Cladding	5 days	Mon 14/09/20	Fri 18/09/20											Electrical				
120		Internal Plastering, Carpentry and Decorating	5 days	Mon 21/09/20	Fri 25/09/20											2nd Fix Pods Internal				
121		External Security Lighting - 2 per property (1 Each to 63 & 65)	3 days	Wed 23/09/20	Fri 25/09/20											Electrical				
122		Clean Gullies	3 days	Wed 23/09/20	Fri 25/09/20											Clean				
123		Clean and Clear Site	1 day	Fri 25/09/20	Fri 25/09/20											Clear Site				
124		Cadman Crescent	26.2 wks	Fri 15/05/20	Tue 17/11/20											Cadman Crescent				
125		1 - 15 Cadman Crescent	22 wks	Fri 15/05/20	Mon 19/10/20											1 - 15 Cadman Crescent				
126		Low Level Works	6.8 wks	Fri 15/05/20	Thu 02/07/20											Low Level Works				
127		Asbestos Works	2 wks	Fri 15/05/20	Mon 01/06/20											Asbestos Works				
130		Remove overhead external door canopies	3 days	Mon 01/06/20	Thu 04/06/20											Asbestos Works				
131		Alter Ramp to allow installation of Pod System/Scaffold No 15	1 day	Thu 04/06/20	Fri 05/06/20											Asbestos Works				
132		Low Level External Enabling (Inc BT, Virgin, Electrical, Grab Rails, Aerials, taps, CCTV, Etc)	4 days	Fri 05/06/20	Thu 11/06/20											Asbestos Works				
133		Low Level Pointing (Inc Brickwork Repairs/Privacy Walls as per BoQ)	16 days	Thu 11/06/20	Thu 02/07/20											Pointing				
134		Install Soffit, Fascia & RWG	16 days	Thu 11/06/20	Thu 02/07/20											Pointing				
135		High Level Works	7.4 wks	Mon 13/07/20	Wed 02/09/20											High Level Works				
136		Erect Scaffold	6 days	Mon 13/07/20	Tue 21/07/20											Erect Scaffold				
137		Asbestos - SVP ET150	1 day	Tue 21/07/20	Wed 22/07/20											Erect Scaffold				
138		Solarplicity Remove Solar Panels (Nos 3, 9, 11 & 15)	1 day	Wed 22/07/20	Thu 23/07/20											Erect Scaffold				
139		HL Brickwork Repointing and Repairs (Inc HL Gables, Stepped Roof Details, Perished Brickwork Etc)	5 days	Thu 23/07/20	Thu 30/07/20											Pointing				
140		Re-Roof (Inc Insulation, Lead, Fire Breaks, Flue Collars, Verge and Eaves Etc)	16 days	Thu 30/07/20	Thu 20/08/20											Roof Renewal				
141		Solarplicity to Refix Solar Panels (Nos 3, 9, 11 & 15)	1 day	Fri 21/08/20	Fri 21/08/20											Roof Renewal				
142		Strike Scaffold	7 days	Mon 24/08/20	Wed 02/09/20											Strike Scaffold				
143		Pods, Kitchens and Bathrooms	3.2 wks	Mon 07/09/20	Mon 28/09/20											Pods, Kitchens and Bathrooms				

Project: Cadman and Adderley Cresce
Date: Mon 11/11/19

Mobilisation/Pre Con

General Construction

Pointing

Scaffolding

Roofing

Pod System

Milestone

Summary

◆

▬

Rolled Up Progress

Project Summary

▬

▬

Group By Summary

Progress

Cadman and Adderley Pre Contract Programme



ID	Task Mode	Name	Duration	Start	Finish	Half 1, 2020							Half 2, 2020							
						N	D	J	F	M	A	M	J	J	A	S	O	N	D	J
144		1 Cadman Crescent	1.2 wks	Mon 07/09/20	Mon 14/09/20												1 Cadman Crescent			
145		Remove Front Façade, Install SFS Frame, External Weatherboarding, Window Frames and External Door	1 day	Mon 07/09/20	Mon 07/09/20												Pod System			
146		Remove Rear Façade, Install SFS Frame, External Weatherboarding, Window Frames and External Door	1 day	Tue 08/09/20	Tue 08/09/20												Pod System			
147		Renew Bathroom	4 days	Wed 09/09/20	Mon 14/09/20												Pod System			
148		3 Cadman Crescent	0.4 wks	Wed 09/09/20	Thu 10/09/20												3 Cadman Crescent			
149		Remove Front Façade, Install SFS Frame, External Weatherboarding, Window Frames and External Door	1 day	Wed 09/09/20	Wed 09/09/20												Pod System			
150		Remove Rear Façade, Install SFS Frame, External Weatherboarding, Window Frames and External Door	1 day	Thu 10/09/20	Thu 10/09/20												Pod System			
151		5 Cadman Crescent	0.4 wks	Fri 11/09/20	Mon 14/09/20												5 Cadman Crescent			
152		Remove Front Façade, Install SFS Frame, External Weatherboarding, Window Frames and External Door	1 day	Fri 11/09/20	Fri 11/09/20												Pod System			
153		Remove Rear Façade, Install SFS Frame, External Weatherboarding, Window Frames and External Door	1 day	Mon 14/09/20	Mon 14/09/20												Pod System			
154		7 Cadman Crescent	0.4 wks	Tue 15/09/20	Wed 16/09/20												7 Cadman Crescent			
155		Remove Front Façade, Install SFS Frame, External Weatherboarding, Window Frames and External Door	1 day	Tue 15/09/20	Tue 15/09/20												Pod System			
156		Remove Rear Façade, Install SFS Frame, External Weatherboarding, Window Frames and External Door	1 day	Wed 16/09/20	Wed 16/09/20												Pod System			
157		9 Cadman Crescent	0.4 wks	Thu 17/09/20	Fri 18/09/20												9 Cadman Crescent			
158		Remove Front Façade, Install SFS Frame, External Weatherboarding, Window Frames and External Door	1 day	Thu 17/09/20	Thu 17/09/20												Pod System			
159		Remove Rear Façade, Install SFS Frame, External Weatherboarding, Window Frames and External Door	1 day	Fri 18/09/20	Fri 18/09/20												Pod System			
160		11 Cadman Crescent	0.4 wks	Mon 21/09/20	Tue 22/09/20												11 Cadman Crescent			
161		Remove Front Façade, Install SFS Frame, External Weatherboarding, Window Frames and External Door	1 day	Mon 21/09/20	Mon 21/09/20												Pod System			
162		Remove Rear Façade, Install SFS Frame, External Weatherboarding, Window Frames and External Door	1 day	Tue 22/09/20	Tue 22/09/20												Pod System			
163		13 Cadman Crescent	0.4 wks	Wed 23/09/20	Thu 24/09/20												13 Cadman Crescent			
164		Remove Front Façade, Install SFS Frame, External Weatherboarding, Window Frames and External Door	1 day	Wed 23/09/20	Wed 23/09/20												Pod System			
165		Remove Rear Façade, Install SFS Frame, External Weatherboarding, Window Frames and External Door	1 day	Thu 24/09/20	Thu 24/09/20												Pod System			
166		15 Cadman Crescent	0.4 wks	Fri 25/09/20	Mon 28/09/20												15 Cadman Crescent			
167		Remove Front Façade, Install SFS Frame, External Weatherboarding, Window Frames and External Door	1 day	Fri 25/09/20	Fri 25/09/20												Pod System			
168		Remove Rear Façade, Install SFS Frame, External Weatherboarding, Window Frames and External Door	1 day	Mon 28/09/20	Mon 28/09/20												Pod System			
169		Rain Defence External Pod Cladding	5 days	Tue 29/09/20	Mon 05/10/20												2nd Fix Pod External			
170		Install Multivent Fans & Ld2s	5 days	Tue 06/10/20	Mon 12/10/20												Electrical			
171		Internal Plastering, Carpentry and Decorating	5 days	Tue 13/10/20	Mon 19/10/20												2nd Fix Pods Internal			
172		External Security Lighting - 1 per property	3 days	Thu 15/10/20	Mon 19/10/20												Electrical			
173		Clean Gullies	3 days	Thu 15/10/20	Mon 19/10/20												Clean			
174		Clean and Clear Site	1 day	Mon 19/10/20	Mon 19/10/20												Clear Site			
175		2-18 Cadman Crescent	23.6 wks	Thu 04/06/20	Tue 17/11/20												2-18 Cadman Crescent			
176		Low Level Works	7.8 wks	Thu 04/06/20	Tue 28/07/20												Low Level Works			
177		Asbestos Works	2.2 wks	Thu 04/06/20	Fri 19/06/20												Asbestos Works			
178		Asbestos - Remove Soffits	9 days	Thu 04/06/20	Wed 17/06/20												Asbestos Works			
179		Asbestos - Packers removal to windows doors and structural timbers	2 days	Wed 17/06/20	Fri 19/06/20												Asbestos Works			
180		Remove overhead external door canopies	2 days	Fri 19/06/20	Tue 23/06/20												Asbestos Works			
181		Alter Ramp to allow installation of Pod System/Scaffold Nos 10, 12, 14, 16, 18	3 days	Tue 23/06/20	Fri 26/06/20												Asbestos Works			
182		Cadent & Gas Works	0.6 wks	Fri 26/06/20	Wed 01/07/20												Cadent & Gas Works			
183		Relocate Gas Meter and Box - 10 Cadman	1 day	Fri 26/06/20	Mon 29/06/20												Cadent & Gas Works			
184		Relocate Gas Meter and Box - 12 Cadman	1 day	Mon 29/06/20	Tue 30/06/20												Cadent & Gas Works			
185		Alter Gas Pipework to allow Pod - 14 Cadman	1 day	Tue 30/06/20	Wed 01/07/20												Cadent & Gas Works			
186		Low Level External Enabling (Inc BT, Virgin, Electrical, Grab Rails, Aerials, taps, CCTv, Etc)	2 days	Wed 01/07/20	Fri 03/07/20												Cadent & Gas Works			
187		Low Level Pointing (Inc Brickwork Repairs/Privacy Walls as per BoQ)	18 days	Fri 03/07/20	Tue 28/07/20												Pointing			

Project: Cadman and Adderley Cresce
Date: Mon 11/11/19

Mobilisation/Pre Con

General Construction

Pointing

Scaffolding

Roofing

Pod System

Milestone

Summary

Rolled Up Progress

Project Summary

Group By Summary

Progress

Cadman and Adderley Pre Contract Programme



ID	Task Name	Mode	Duration	Start	Finish	Half 1, 2020							Half 2, 2020								
						N	D	J	F	M	A	M	J	J	A	S	O	N	D		J
188	Install Soffit, Fascia & RWG		18 days	Fri 03/07/20	Tue 28/07/20																
189	High Level Works		8.8 wks	Wed 29/07/20	Tue 29/09/20																
190	Erect Scaffold		9 days	Wed 29/07/20	Tue 11/08/20																
191	Asbestos - SVP ET150		1 day	Tue 11/08/20	Wed 12/08/20																
192	Solarplicity Remove Solar Panels (No 8)		1 day	Wed 12/08/20	Thu 13/08/20																
193	HL Brickwork Repointing and Repairs (Inc HL Gables, Stepped Roof Details, Perished Brickwork Etc)		6 days	Thu 13/08/20	Fri 21/08/20																
194	Re-Roof (Inc Insulation, Lead, Fire Breaks, Flue Collars, Verge and Eaves Etc)		18 days	Fri 21/08/20	Wed 16/09/20																
195	Solarplicity to Refix Solar Panels (No 8)		1 day	Thu 17/09/20	Thu 17/09/20																
196	Strike Scaffold		8 days	Fri 18/09/20	Tue 29/09/20																
197	Pods, Kitchens and Bathrooms		4.4 wks	Tue 29/09/20	Wed 28/10/20																
198	2 Cadman Crescent		0.4 wks	Tue 29/09/20	Wed 30/09/20																
199	Remove Front Façade, Install SFS Frame, External Weatherboarding, Window Frames and External Door		1 day	Tue 29/09/20	Tue 29/09/20																
200	Remove Rear Façade, Install SFS Frame, External Weatherboarding, Window Frames and External Door		1 day	Wed 30/09/20	Wed 30/09/20																
201	4 Cadman Crescent		0.4 wks	Thu 01/10/20	Fri 02/10/20																
202	Remove Front Façade, Install SFS Frame, External Weatherboarding, Window Frames and External Door		1 day	Thu 01/10/20	Thu 01/10/20																
203	Remove Rear Façade, Install SFS Frame, External Weatherboarding, Window Frames and External Door		1 day	Fri 02/10/20	Fri 02/10/20																
204	6 Cadman Crescent		0.4 wks	Mon 05/10/20	Tue 06/10/20																
205	Remove Front Façade, Install SFS Frame, External Weatherboarding, Window Frames and External Door		1 day	Mon 05/10/20	Mon 05/10/20																
206	Remove Rear Façade, Install SFS Frame, External Weatherboarding, Window Frames and External Door		1 day	Tue 06/10/20	Tue 06/10/20																
207	8 Cadman Crescent		1.2 wks	Wed 07/10/20	Wed 14/10/20																
208	Remove Front Façade, Install SFS Frame, External Weatherboarding, Window Frames and External Door		1 day	Wed 07/10/20	Wed 07/10/20																
209	Remove Rear Façade, Install SFS Frame, External Weatherboarding, Window Frames and External Door		1 day	Thu 08/10/20	Thu 08/10/20																
210	Renew Kitchen		4 days	Fri 09/10/20	Wed 14/10/20																
211	10 Cadman Crescent		0.4 wks	Thu 15/10/20	Fri 16/10/20																
212	Remove Front Façade, Install SFS Frame, External Weatherboarding, Window Frames and External Door		1 day	Thu 15/10/20	Thu 15/10/20																
213	Remove Rear Façade, Install SFS Frame, External Weatherboarding, Window Frames and External Door		1 day	Fri 16/10/20	Fri 16/10/20																
214	12 Cadman Crescent		1.2 wks	Mon 19/10/20	Mon 26/10/20																
215	Remove Front Façade, Install SFS Frame, External Weatherboarding, Window Frames and External Door		1 day	Mon 19/10/20	Mon 19/10/20																
216	Remove Rear Façade, Install SFS Frame, External Weatherboarding, Window Frames and External Door		1 day	Tue 20/10/20	Tue 20/10/20																
217	Renew Bathroom		4 days	Wed 21/10/20	Mon 26/10/20																
218	14 Cadman Crescent		0.4 wks	Wed 21/10/20	Thu 22/10/20																
219	Remove Front Façade, Install SFS Frame, External Weatherboarding, Window Frames and External Door		1 day	Wed 21/10/20	Wed 21/10/20																
220	Remove Rear Façade, Install SFS Frame, External Weatherboarding, Window Frames and External Door		1 day	Thu 22/10/20	Thu 22/10/20																
221	16 Cadman Crescent		0.4 wks	Fri 23/10/20	Mon 26/10/20																
222	Remove Front Façade, Install SFS Frame, External Weatherboarding, Window Frames and External Door		1 day	Fri 23/10/20	Fri 23/10/20																
223	Remove Rear Façade, Install SFS Frame, External Weatherboarding, Window Frames and External Door		1 day	Mon 26/10/20	Mon 26/10/20																
224	18 Cadman Crescent		0.4 wks	Tue 27/10/20	Wed 28/10/20																
225	Remove Front Façade, Install SFS Frame, External Weatherboarding, Window Frames and External Door		1 day	Tue 27/10/20	Tue 27/10/20																
226	Remove Rear Façade, Install SFS Frame, External Weatherboarding, Window Frames and External Door		1 day	Wed 28/10/20	Wed 28/10/20																
227	Rain Defence External Pod Cladding		5 days	Wed 28/10/20	Tue 03/11/20																
228	Install Multivent Fans & Ld2s		5 days	Wed 04/11/20	Tue 10/11/20																
229	Internal Plastering, Carpentry and Decorating		5 days	Wed 11/11/20	Tue 17/11/20																
230	External Security Lighting - 1 per property		3 days	Fri 13/11/20	Tue 17/11/20																
231	Clean Gullies		3 days	Fri 13/11/20	Tue 17/11/20																

Project: Cadman and Adderley Cresce
Date: Mon 11/11/19

Mobilisation/Pre Con

General Construction

Pointing

Scaffolding

Roofing

Pod System

Milestone

Summary

◆

◆

Rolled Up Progress

Project Summary

Group By Summary

Progress



ID	Task Mode	Name	Duration	Start	Finish			Half 1, 2020						Half 2, 2020						
						N	D	J	F	M	A	M	J	J	A	S	O	N	D	
232		Clean and Clear Site	1 day	Tue 17/11/20	Tue 17/11/20			J	F	M	A	M	J	J	A	S	O	N	D	J

Clear Site
