Programme of Works - Edginswell Wickes Project
Rev 2 12/05/2021
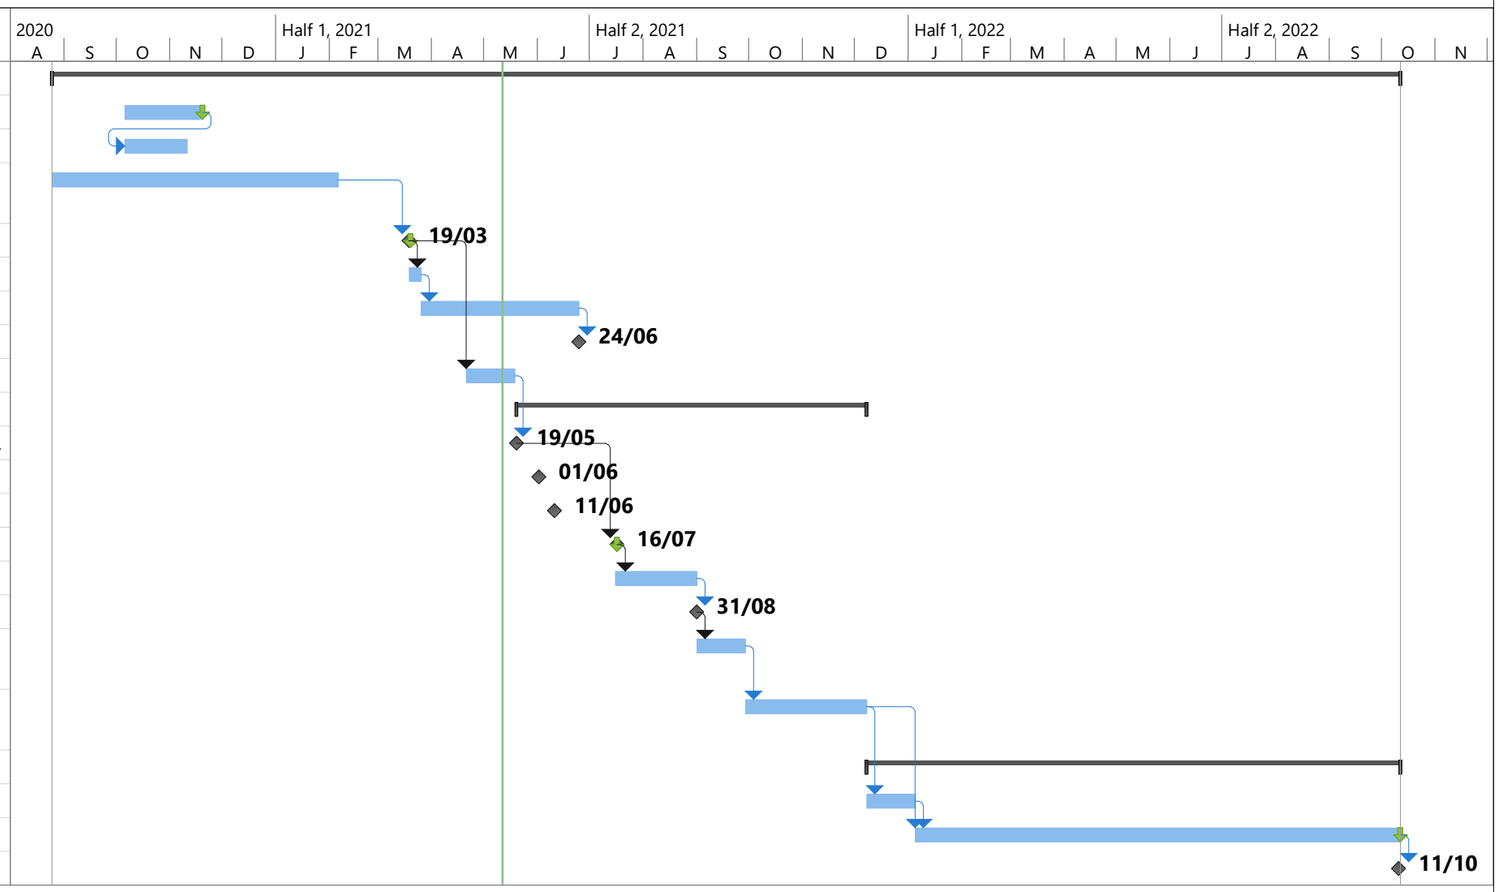
ID		Task Name	Start	Finish
1		**Retail Project (Wickes)**	**Tue 25/08/20**	**Tue 11/10/22**
2		Retail project initial design team appointed	Tue 06/10/20	Thu 19/11/20
3		EOI received for Retail Project	Tue 06/10/20	Tue 10/11/20
4		Retail project complete Agreement for Lease	Tue 25/08/20	Fri 05/02/21
5		Retail project planning submitted	Fri 19/03/21	Fri 19/03/21
6		Planning validation	Fri 19/03/21	Thu 25/03/21
7		Planning period	Fri 26/03/21	Thu 24/06/21
8		Planning granted	Thu 24/06/21	Thu 24/06/21
9		Finalising Tender Pack	Wed 21/04/21	Tue 18/05/21
10		**Tender Period**	**Wed 19/05/21**	**Tue 07/12/21**
11		MC2 Issued to SCF Framework	Wed 19/05/21	Wed 19/05/21
12		Site visit 12:00	Tue 01/06/21	Tue 01/06/21
13		Clarification Deadline	Fri 11/06/21	Fri 11/06/21
14		Retail project tenders received	Fri 16/07/21	Fri 16/07/21
15		Tender Evaluation	Fri 16/07/21	Tue 31/08/21
16		Notification letters to contractors	Tue 31/08/21	Tue 31/08/21
17		Entering into Contract with successful contractor	Wed 01/09/21	Tue 28/09/21
18		RIBA Stage 4 design (Undertaken by the selected contractor)	Wed 29/09/21	Tue 07/12/21
19		**Construction**	**Wed 08/12/21**	**Tue 11/10/22**
20		Contractor Mobilisation	Wed 08/12/21	Tue 04/01/22
21		Retail project works on site	Wed 05/01/22	Tue 11/10/22
22		PC Retail project	Tue 11/10/22	Tue 11/10/22
